





Actual Level of Effort Remaining Work Milestone
Actual Work Critical Remaining Work summary

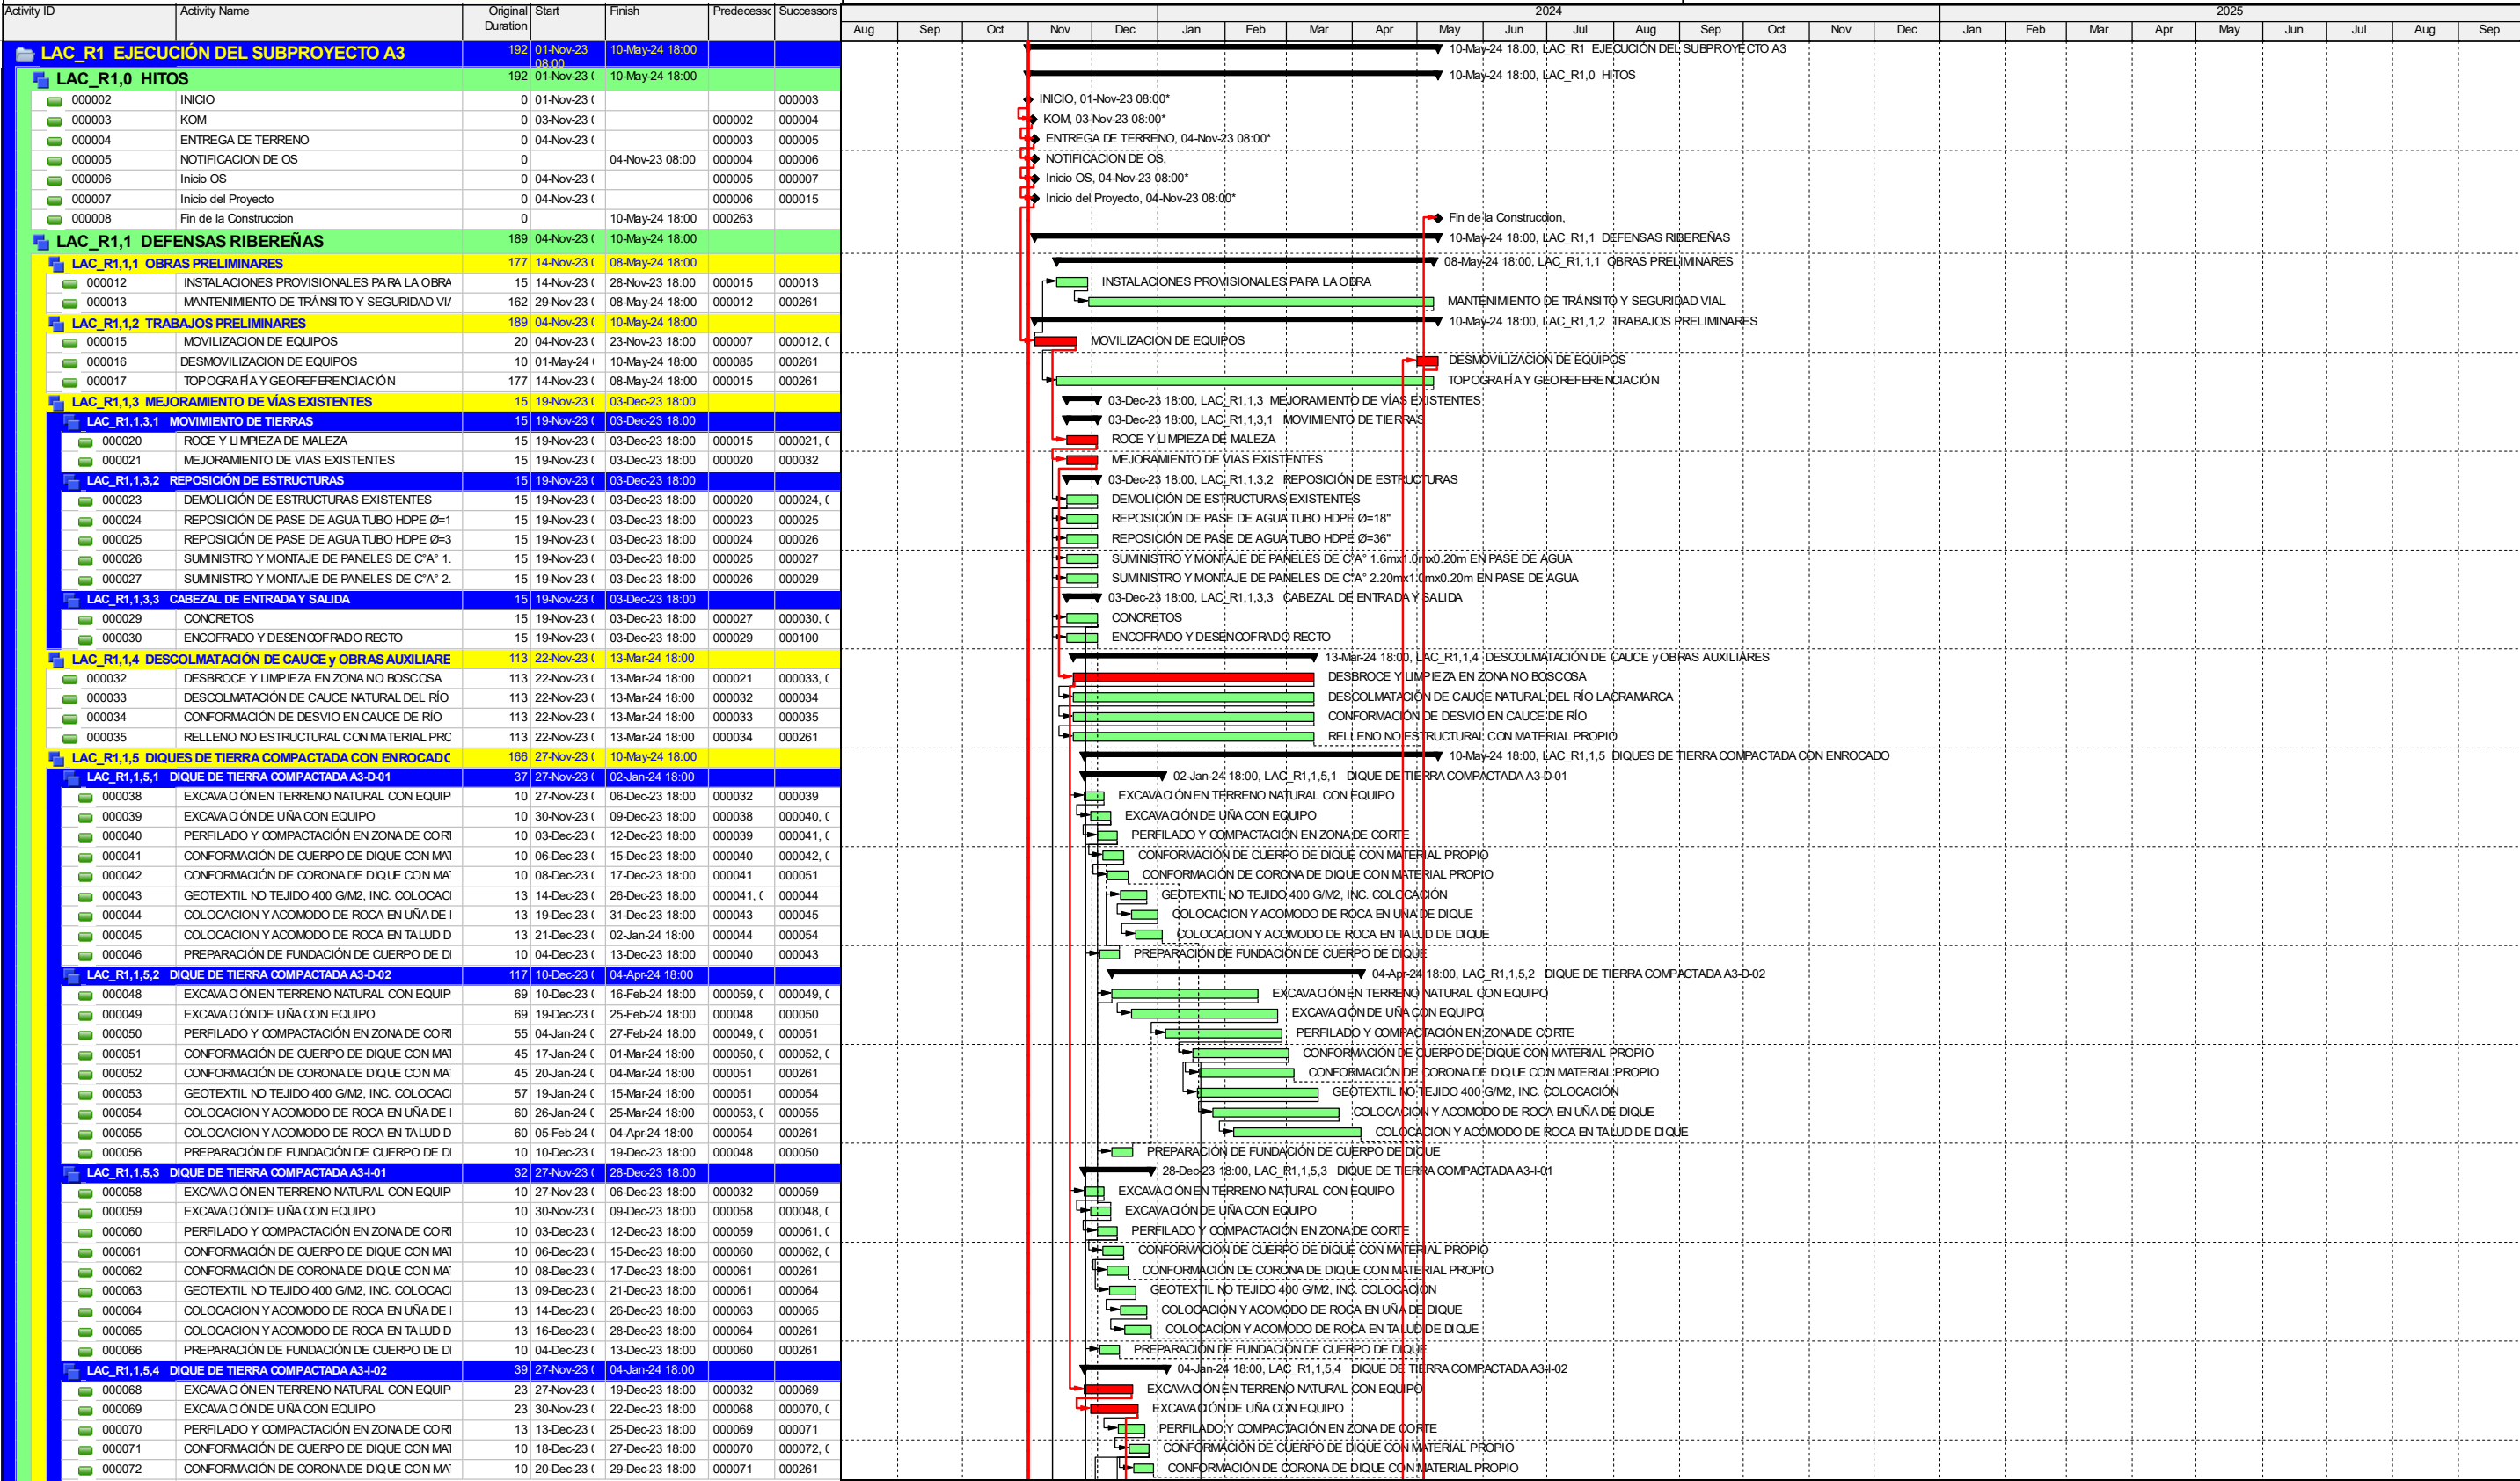


SUBCONTRATACIÓN DEL SUB PROYECTO A3 - RÍO LACRAMARCA

07-Oct-23 22:27

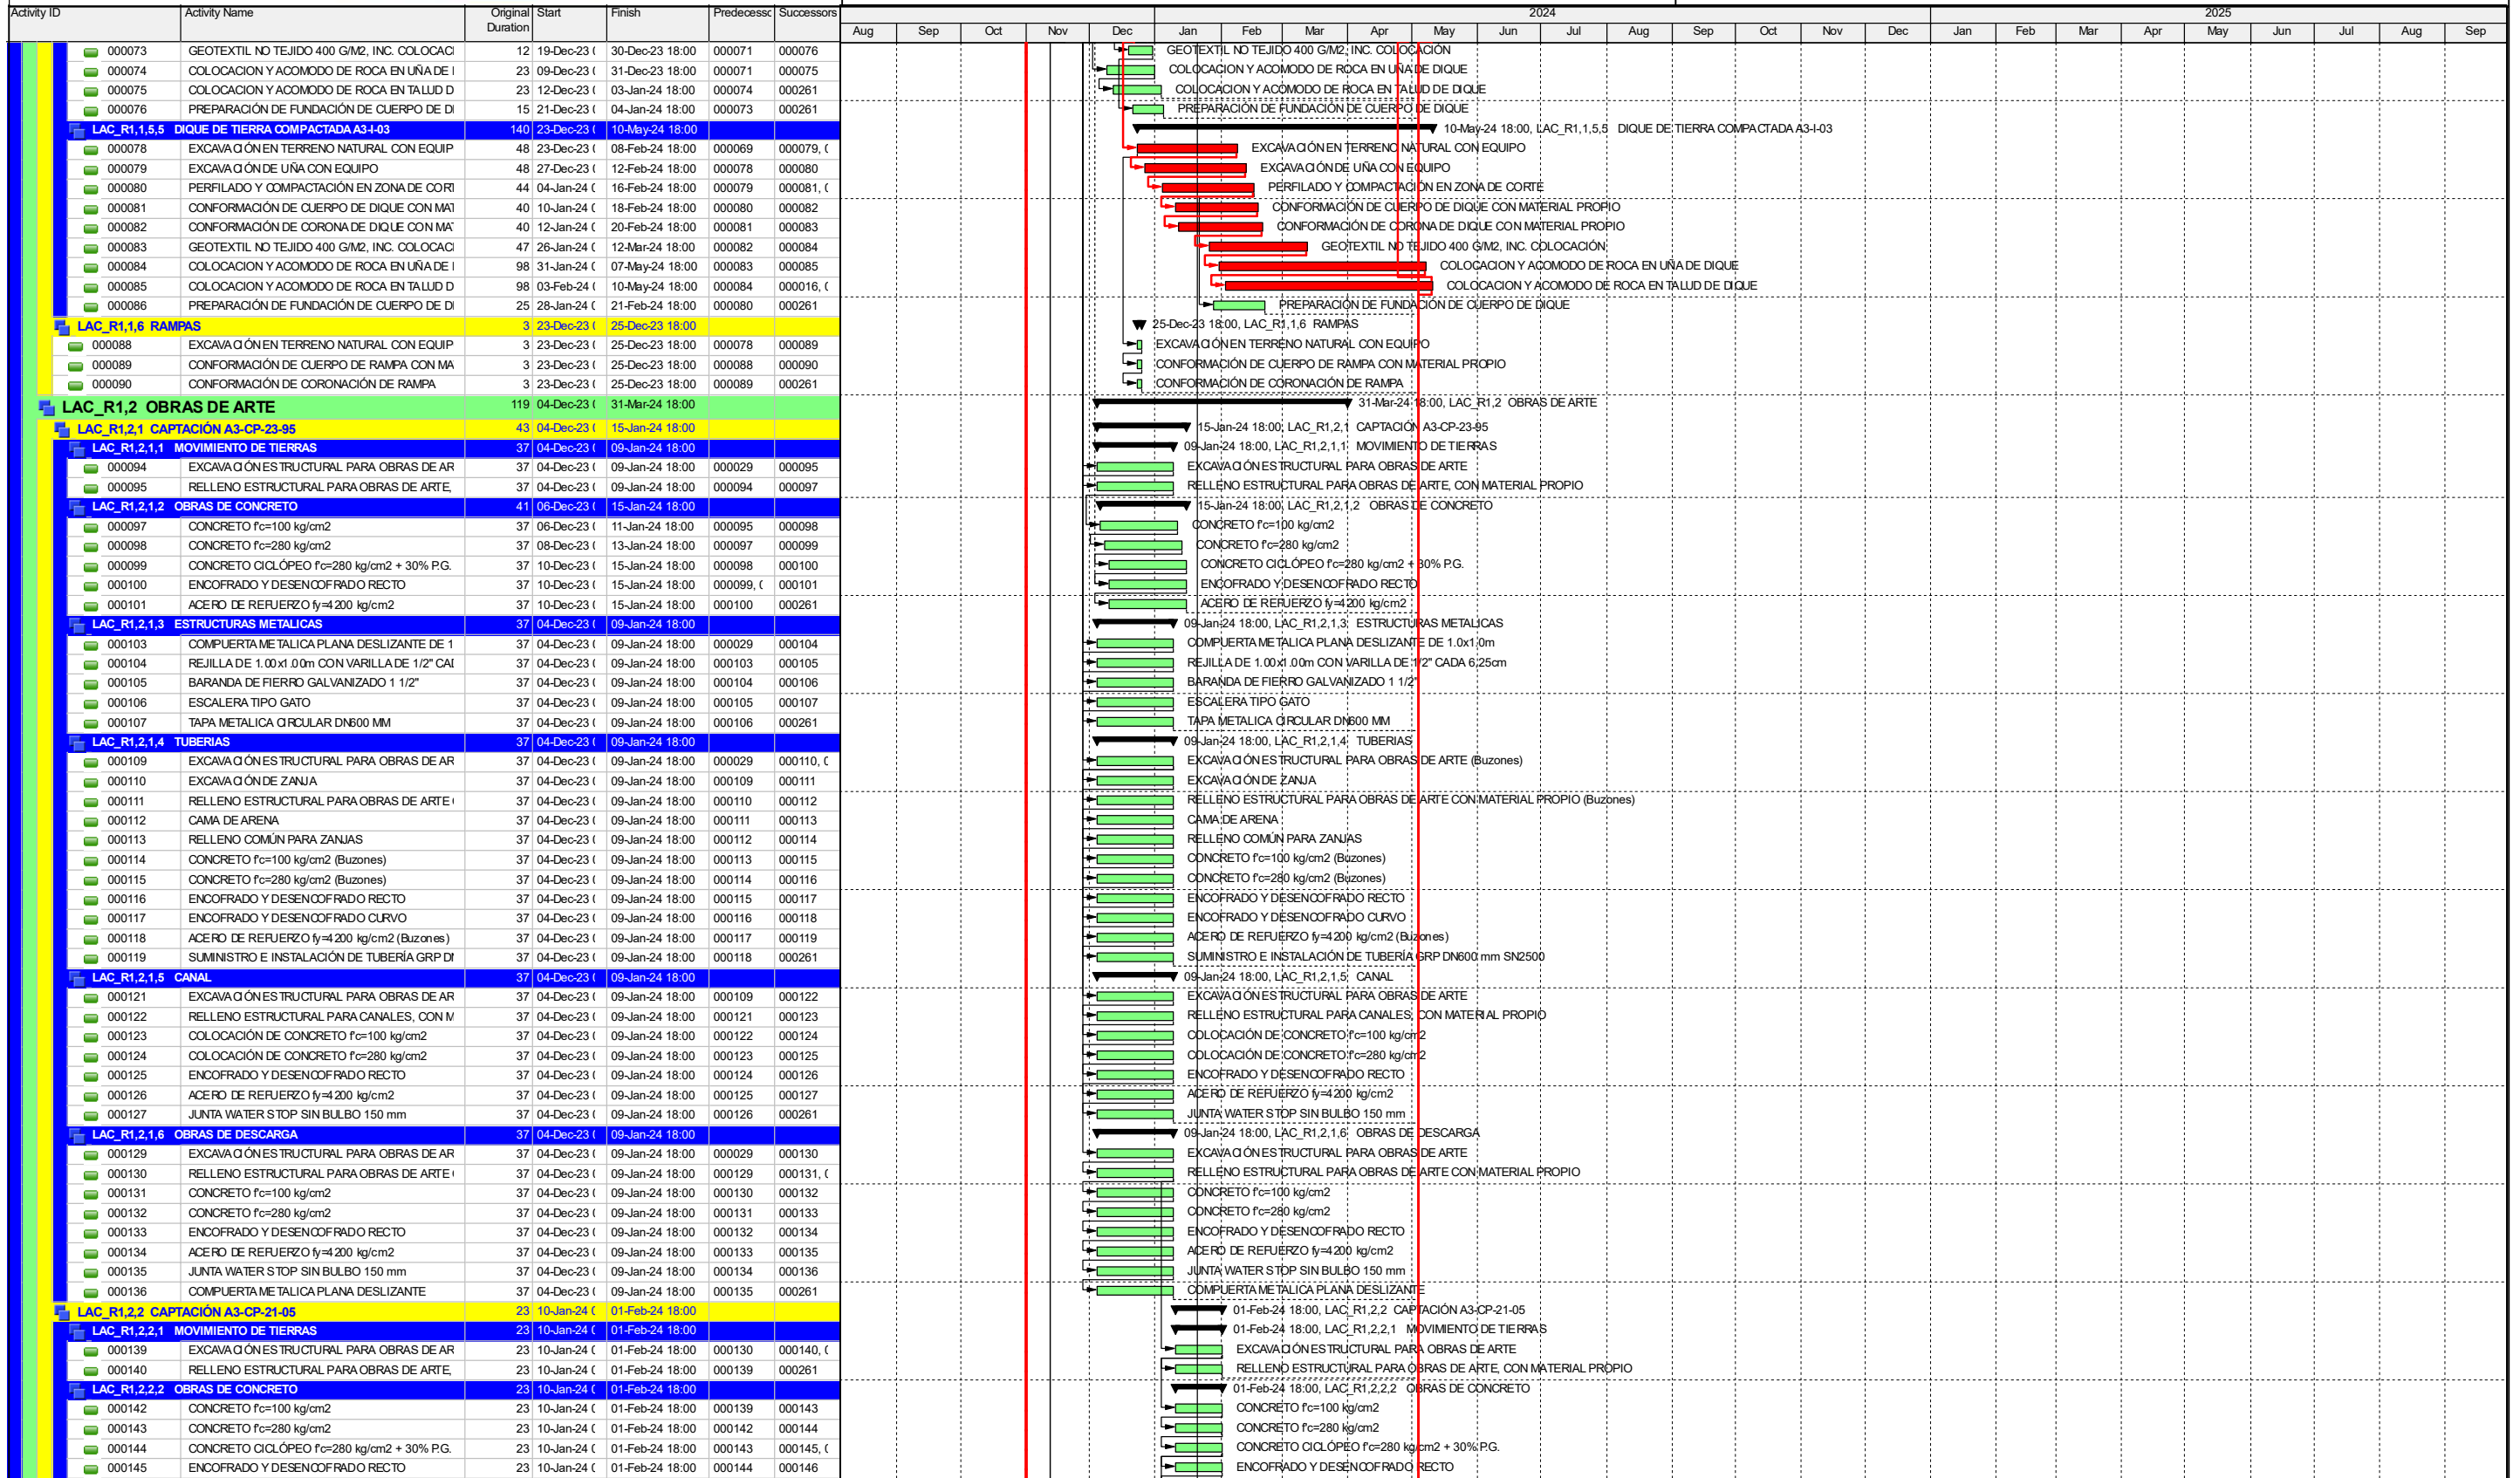

Actual Level of Effort Remaining Work Milestone
Actual Work Critical Remaining Work summary



© Oracle Corporation



Activity ID	Activity Name	Original Duration	Start	Finish	Predecessors	Successors	2024												2025												
							Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
000219	RELLENO COMÚN	13	23-Jan-24	04-Feb-24 18:00	000218	000220																									
	TUBERÍAS DE 14" HDPE SDR21 DN 355mm	13	21-Jan-24	02-Feb-24 18:00	000219	000221																									
	CONCRETO f'c=100 kg/cm2	13	19-Jan-24	31-Jan-24 18:00	000220	000222																									
	CONCRETO f'c=280 kg/cm2	13	17-Jan-24	29-Jan-24 18:00	000221	000223																									
	ENCOFRADO Y DESENCOFRADO RECTO	13	15-Jan-24	27-Jan-24 18:00	000222	000224																									
	ACERO DE REFUERZO fy=4200 kg/cm2	13	13-Jan-24	25-Jan-24 18:00	000223	000225																									
	CODOS HDPE DE 14" DN 355mm	13	11-Jan-24	23-Jan-24 18:00	000224	000261																									
LAC_R1,3	TRANSPORTE DE MATERIAL	176	15-Nov-23	08-May-24 18:00																											
000227	TRANSPORTE DE MATERIAL GRANULAR PARA DISTANCIAS <1KM	172	19-Nov-23	08-May-24 18:00	000023	000228, (																									
000228	TRANSPORTE DE MATERIAL GRANULAR PARA DISTANCIAS >1KM	172	17-Nov-23	06-May-24 18:00	000227	000229																									
000229	TRANSPORTE DE ROCA PARA DISTANCIAS <1KM	172	15-Nov-23	04-May-24 18:00	000228	000261																									
000230	TRANSPORTE DE ROCA PARA DISTANCIAS >1KM	172	19-Nov-23	08-May-24 18:00	000227	000261																									
000231	TRANSPORTE DE MATERIAL EXCEDENTE PARA DISTANCIAS <1KM	172	19-Nov-23	08-May-24 18:00	000227	000261																									
000232	TRANSPORTE DE MATERIAL EXCEDENTE PARA DISTANCIAS >1KM	172	19-Nov-23	08-May-24 18:00	000227	000261																									
LAC_R1,4	ARQUITECTURA Y PAISAJISMO	18	19-Nov-23	06-Dec-23 18:00																											
LAC_R1,4.1	OBRAS PRELIMINARES	18	19-Nov-23	06-Dec-23 18:00																											
000235	MOVILIZACIÓN Y DEMOVILIZACIÓN DE EQUIPOS Y HERRAMIENTAS (ARQUITECTURA Y PAISAJISMO)	18	19-Nov-23	06-Dec-23 18:00	000227	000236, (																									
000236	TRAZO Y REPLANTEO PRELIMINAR	18	19-Nov-23	06-Dec-23 18:00	000235	000261																									
LAC_R1,4.2	MOVIMIENTO DE TIERRAS	18	19-Nov-23	06-Dec-23 18:00																											
000238	EXCAVACIÓN MANUAL PARA INSTALACIÓN DE BORDILLOS Y CIMENTACIONES	18	19-Nov-23	06-Dec-23 18:00	000235	000239																									
000239	EXCAVACIÓN PARA MEJORAMIENTO DE SUELO CON TIERRA VEGETAL	18	19-Nov-23	06-Dec-23 18:00	000238	000240, (																									
000240	ELIMINACIÓN DE MATERIAL EXCEDENTE (DME'S)	18	19-Nov-23	06-Dec-23 18:00	000239	000261																									
LAC_R1,4.3	PAVIMENTOS, RECUBRIMIENTOS Y BORDILLOS	18	19-Nov-23	06-Dec-23 18:00																											
000242	PISO DE GRAVILLA	18	19-Nov-23	06-Dec-23 18:00	000239	000243																									
000243	RECUBRIMIENTO DE PIEDRA DEL LUGAR e=0.05cm	18	19-Nov-23	06-Dec-23 18:00	000242	000244, (																									
000244	BORDILLOS DE PIEDRA DEL LUGAR	18	19-Nov-23	06-Dec-23 18:00	000243	000261																									
LAC_R1,4.4	MOBILIARIOS, BARANDAS Y ESCALERAS	18	19-Nov-23	06-Dec-23 18:00																											
000246	ESCALERA DE CONCRETO SOBRE ENROCADO, CIMENTACIÓN Y ANCLAJE	18	19-Nov-23	06-Dec-23 18:00	000243	000247																									
000247	BARANDA DE MADERA EUCALIPTO CON SOGA, INCLUYE CIMENTACIÓN	18	19-Nov-23	06-Dec-23 18:00	000246	000248																									
000248	TACHOS DE BASURA, INCLUYE CIMENTACIÓN	18	19-Nov-23	06-Dec-23 18:00	000247	000249																									
000249	BANCAS DE CONCRETO, INCLUYE CIMENTACIÓN	18	19-Nov-23	06-Dec-23 18:00	000248	000250																									
000250	POSTES DE ILUMINACIÓN, INCLUYE LUMINARIA Y CIMENTACIÓN	18	19-Nov-23	06-Dec-23 18:00	000249	000251																									
000251	SEÑALÉTICA INFORMATIVA	18	19-Nov-23	06-Dec-23 18:00	000250	000252																									
000252	BOLARDOS DE PIEDRA	18	19-Nov-23	06-Dec-23 18:00	000251	000261																									
LAC_R1,4.5	INSTALACION DE ALCORQUES	2	19-Nov-23	20-Nov-23 18:00																											
000254	ALCORQUES DE PIEDRA DE CANTO RODADO PARA ARBOLES	2	19-Nov-23	20-Nov-23 18:00	000235	000261																									
LAC_R1,5	PROGRAMA DE CIERRE DE OBRA	172	19-Nov-23	08-May-24 18:00																											
000256	ACONDICIONAMIENTO DE DEPÓSITOS DE MATERIALES EXCEDENTES (DME)	172	19-Nov-23	08-May-24 18:00	000023	000257, (																									
000257	RESTAURACIÓN DE ÁREAS DE INSTALACIONES PROVISIONALES	172	19-Nov-23	08-May-24 18:00	000256	000261																									
LAC_R1,6	SEGURIDAD Y SALUD OCUPACIONAL	172	19-Nov-23	08-May-24 18:00																											
000259	SEGURIDAD Y SALUD OCUPACIONAL	172	19-Nov-23	08-May-24 18:00	000256	000261																									
LAC_R1,7	LIMPIEZA Y ENTREGA	10	01-May-24	10-May-24 18:00																											
000261	TERMINO DE LOS TRABAJOS	0		10-May-24 18:00	000259, (	000262																									
000262	LIMPIEZA DEL SITIO	10	01-May-24	10-May-24 18:00	000261	000263																									
000263	ENTREGA	0		10-May-24 18:00	000262	000008																									
