


CURVA S - RELLENOS																															
CLIENTE	OHLA																														
CONTRATISTA	AJANI SAC																														
PROYECTO	SUB PROYECTO A3																														
INICIO CONSTRUCCIÓN	18/05/2023																														
FIN CONTRUCCIÓN	2/12/2023																														



	S1	S2	S3	S4	S5	S6	S7	S8	S9	S10	S11	S12	S13	S14	S15	S16	S17	S18	S19	S20	S21	S22	S23	S24	S25	S26	S27	S28	S29	S30	S31	S32
	24/04/2023	1/05/2023	8/05/2023	15/05/2023	22/05/2023	29/05/2023	5/06/2023	12/06/2023	19/06/2023	26/06/2023	3/07/2023	10/07/2023	17/07/2023	24/07/2023	31/07/2023	7/08/2023	14/08/2023	21/08/2023	28/08/2023	4/09/2023	11/09/2023	18/09/2023	25/09/2023	2/10/2023	9/10/2023	16/10/2023	23/10/2023	30/10/2023	6/11/2023	13/11/2023	20/11/2023	27/11/2023
	30/04/2023	7/05/2023	14/05/2023	21/05/2023	28/05/2023	4/06/2023	11/06/2023	18/06/2023	25/06/2023	2/07/2023	9/07/2023	16/07/2023	23/07/2023	30/07/2023	6/08/2023	13/08/2023	20/08/2023	27/08/2023	3/09/2023	10/09/2023	17/09/2023	24/09/2023	1/10/2023	8/10/2023	15/10/2023	22/10/2023	29/10/2023	5/11/2023	12/11/2023	19/11/2023	26/11/2023	3/12/2023
Línea Base 0_Early	0	0	0	0	0	0	0	1639.2	2689.84	672.46	1115.47	1731.22	3061.93	3380.35	449.99	64.28	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Línea Base 0_Acum. Early	0	0	0	0	0	0	0	1639.2	4329.04	5001.5	6116.97	7848.19	10910.12	14290.47	14740.46	14804.74	14804.74	14804.74	14804.74	14804.74	14804.74	14804.74	14804.74	14804.74	14804.74	14804.74	14804.74	14804.74	14804.74	14804.74	14804.74	14804.74
% Línea Base 0_Acum. Early	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	11.07%	29.24%	33.78%	41.32%	53.01%	73.69%	96.53%	99.57%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%

Curva S - Subproyecto A3

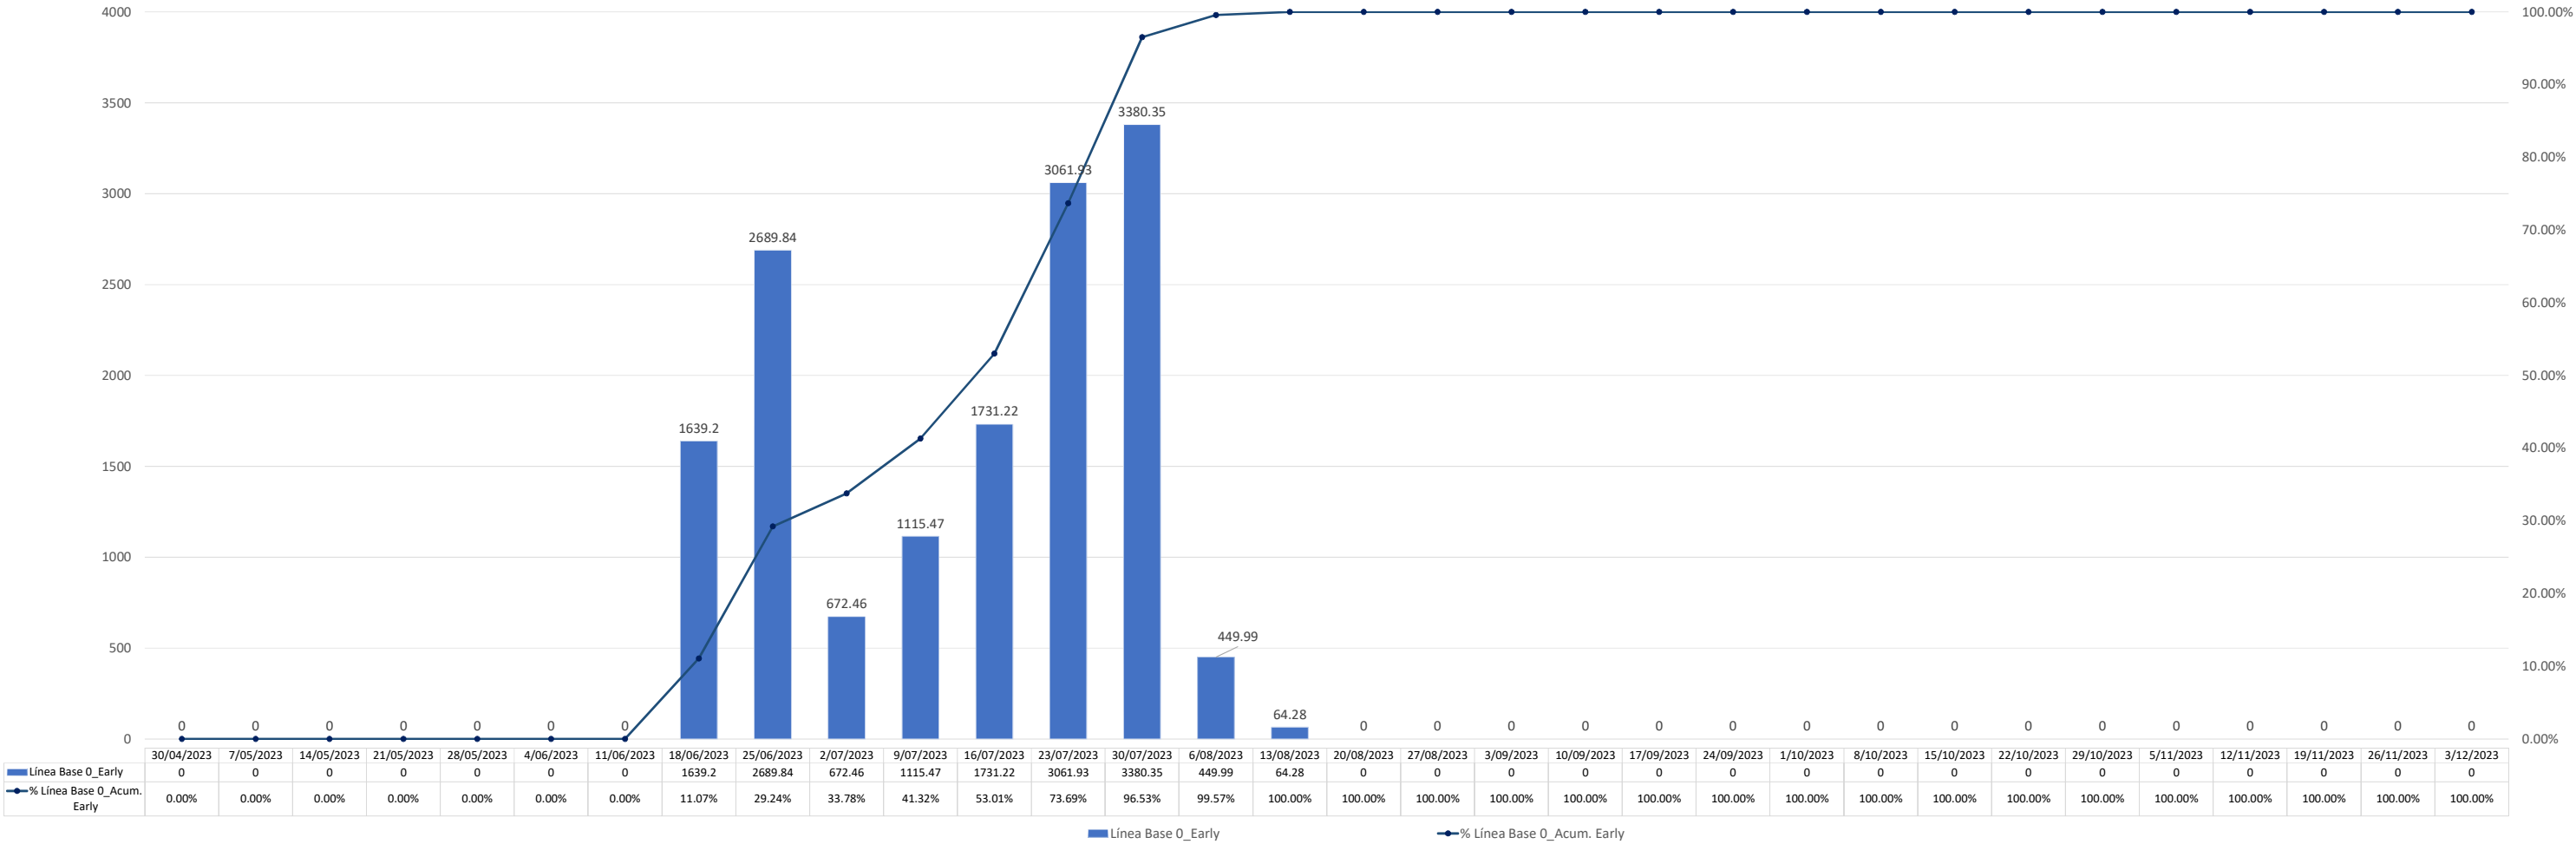


CURVA S - EXCAVACIONES																															
CLIENTE	OHLA																														
CONTRATISTA	AJANI SAC																														
PROYECTO	SUB PROYECTO A3																														
INICIO CONSTRUCCIÓN	18/05/2023																														
FIN CONTRUCCIÓN	2/12/2023																														



	S1	S2	S3	S4	S5	S6	S7	S8	S9	S10	S11	S12	S13	S14	S15	S16	S17	S18	S19	S20	S21	S22	S23	S24	S25	S26	S27	S28	S29	S30	S31	S32
	24/04/2023	1/05/2023	8/05/2023	15/05/2023	22/05/2023	29/05/2023	5/06/2023	12/06/2023	19/06/2023	26/06/2023	3/07/2023	10/07/2023	17/07/2023	24/07/2023	31/07/2023	7/08/2023	14/08/2023	21/08/2023	28/08/2023	4/09/2023	11/09/2023	18/09/2023	25/09/2023	2/10/2023	9/10/2023	16/10/2023	23/10/2023	30/10/2023	6/11/2023	13/11/2023	20/11/2023	27/11/2023
	30/04/2023	7/05/2023	14/05/2023	21/05/2023	28/05/2023	4/06/2023	11/06/2023	18/06/2023	25/06/2023	2/07/2023	9/07/2023	16/07/2023	23/07/2023	30/07/2023	6/08/2023	13/08/2023	20/08/2023	27/08/2023	3/09/2023	10/09/2023	17/09/2023	24/09/2023	1/10/2023	8/10/2023	15/10/2023	22/10/2023	29/10/2023	5/11/2023	12/11/2023	19/11/2023	26/11/2023	3/12/2023
Línea Base 0_Early	0	0	0	0	7313.26	12529.38	6204.05	7941.17	25869.75	37204.61	21216.36	15616.95	11702.76	8046.24	8800.7	2275.54	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Línea Base 0_Acum. Early	0	0	0	0	7313.26	19842.64	26046.69	33987.86	59857.61	97062.22	118278.58	133895.53	145598.29	153644.53	162445.23	164720.77	164720.77	164720.77	164720.77	164720.77	164720.77	164720.77	164720.77	164720.77	164720.77	164720.77	164720.77	164720.77	164720.77	164720.77	164720.77	164720.77
% Línea Base 0_Acum. Early	0.00%	0.00%	0.00%	0.00%	4.44%	12.05%	15.81%	20.63%	36.34%	58.93%	71.81%	81.29%	88.39%	93.28%	98.62%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%

Curva S - Subproyecto A3

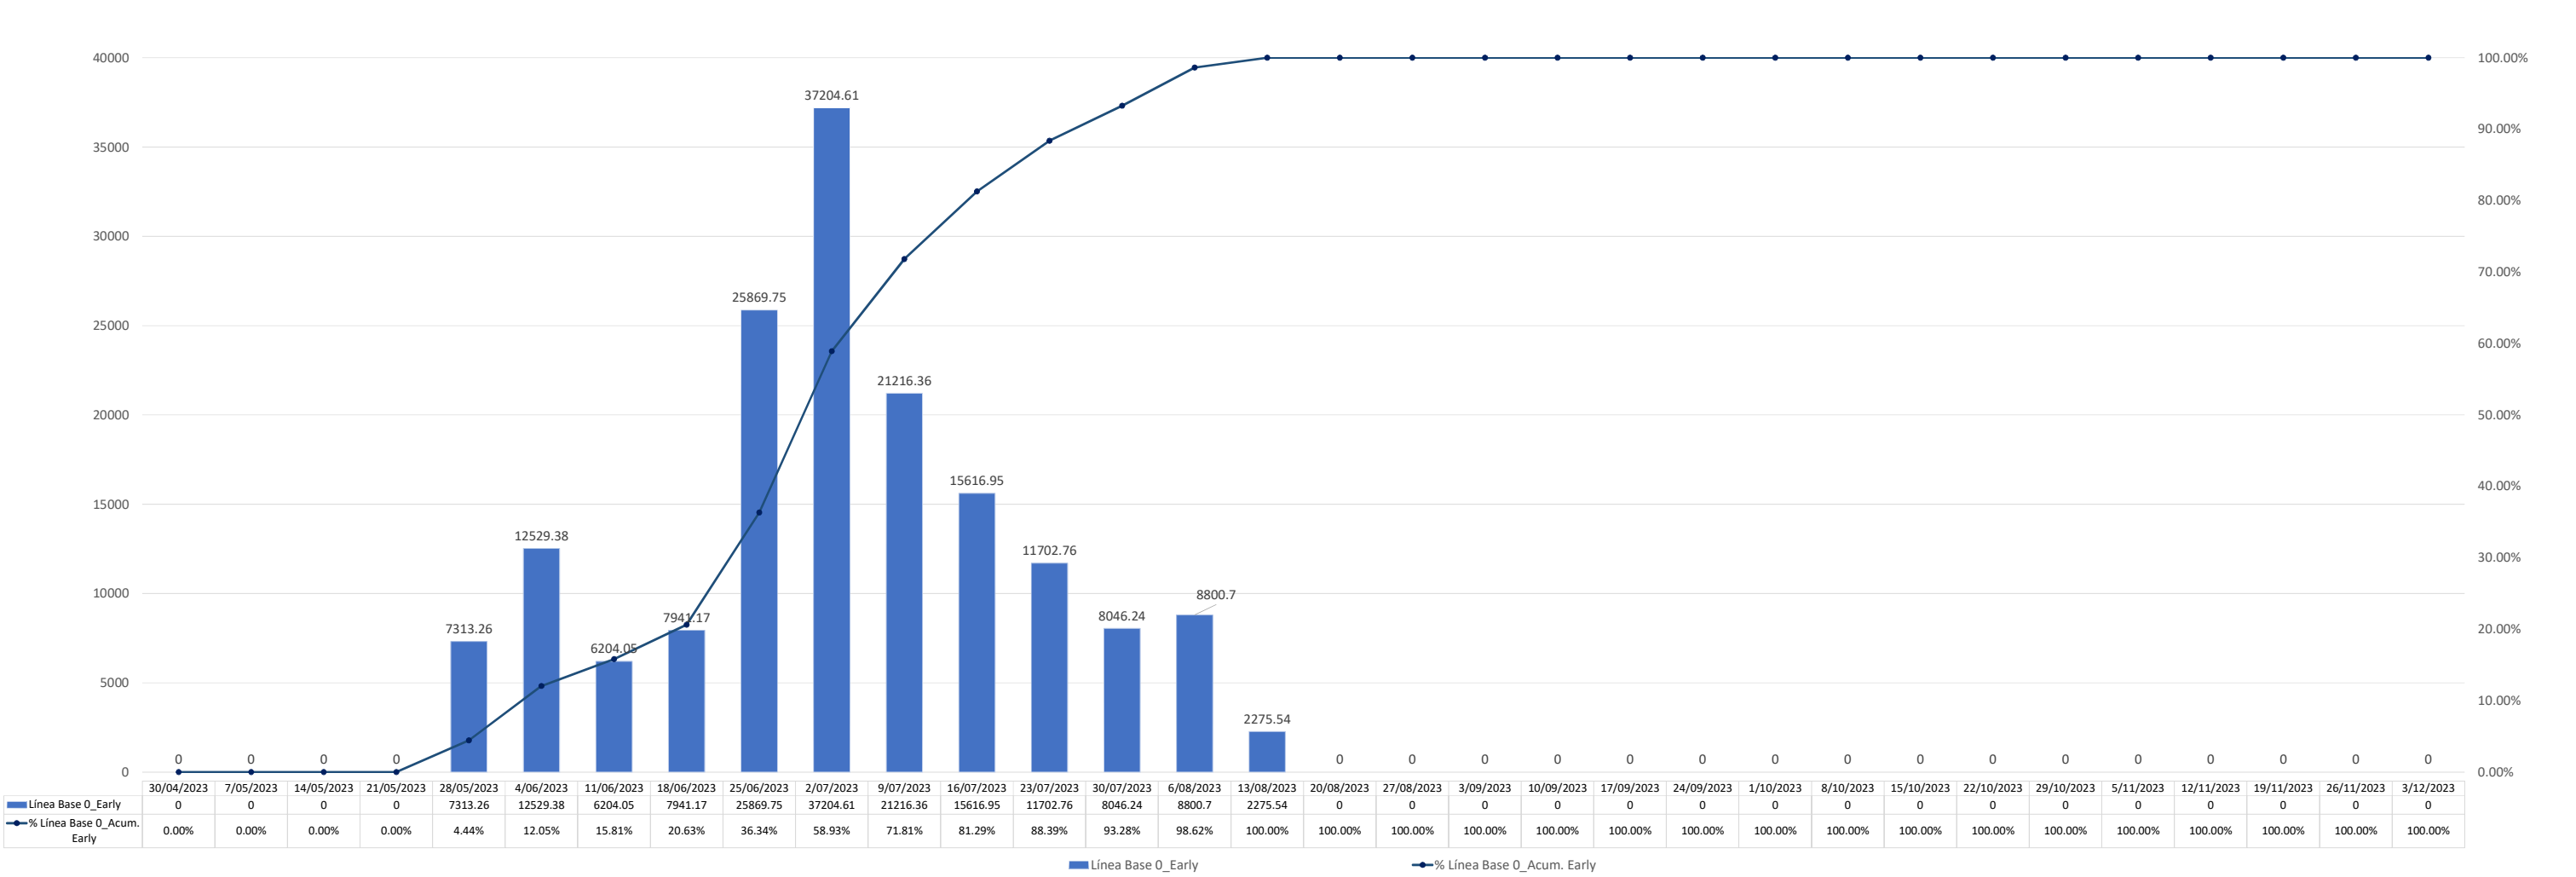

CURVA S - ENROCADO																															
CLIENTE	OHLA																														
CONTRATISTA	AJANI SAC																														
PROYECTO	SUB PROYECTO A3																														
INICIO CONSTRUCCIÓN	18/05/2023																														
FIN CONTRUCCION	2/12/2023																														



	S1	S2	S3	S4	S5	S6	S7	S8	S9	S10	S11	S12	S13	S14	S15	S16	S17	S18	S19	S20	S21	S22	S23	S24	S25	S26	S27	S28	S29	S30	S31	S32
	24/04/2023	1/05/2023	8/05/2023	15/05/2023	22/05/2023	29/05/2023	5/06/2023	12/06/2023	19/06/2023	26/06/2023	3/07/2023	10/07/2023	17/07/2023	24/07/2023	31/07/2023	7/08/2023	14/08/2023	21/08/2023	28/08/2023	4/09/2023	11/09/2023	18/09/2023	25/09/2023	2/10/2023	9/10/2023	16/10/2023	23/10/2023	30/10/2023	6/11/2023	13/11/2023	20/11/2023	27/11/2023
	30/04/2023	7/05/2023	14/05/2023	21/05/2023	28/05/2023	4/06/2023	11/06/2023	18/06/2023	25/06/2023	2/07/2023	9/07/2023	16/07/2023	23/07/2023	30/07/2023	6/08/2023	13/08/2023	20/08/2023	27/08/2023	3/09/2023	10/09/2023	17/09/2023	24/09/2023	1/10/2023	8/10/2023	15/10/2023	22/10/2023	29/10/2023	5/11/2023	12/11/2023	19/11/2023	26/11/2023	3/12/2023
Línea Base 0_Early	0	0	0	0	0	0	0	0	715.39	1251.93	2583.6	2912.14	3960.44	7199.3	8839.38	11570.88	10926.17	9956.34	8123.56	6366.75	4921.49	3893.82	2794.95	1880.09	906.91	0	0	0	0	0	0	0
Línea Base 0_Acum. Early	0	0	0	0	0	0	0	0	715.39	1967.32	4550.92	7463.06	11423.5	18622.8	27462.18	39033.06	49959.23	59915.57	68039.13	74405.88	79327.37	83221.19	86016.14	87896.23	88803.14	88803.14	88803.14	88803.14	88803.14	88803.14	88803.14	88803.14
% Línea Base 0_Acum. Early	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.00%	0.81%	2.22%	5.12%	8.40%	12.86%	20.97%	30.92%	43.95%	56.26%	67.47%	76.62%	83.79%	89.33%	93.71%	96.86%	98.98%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%	100.00%

Curva S - Subproyecto A3

