
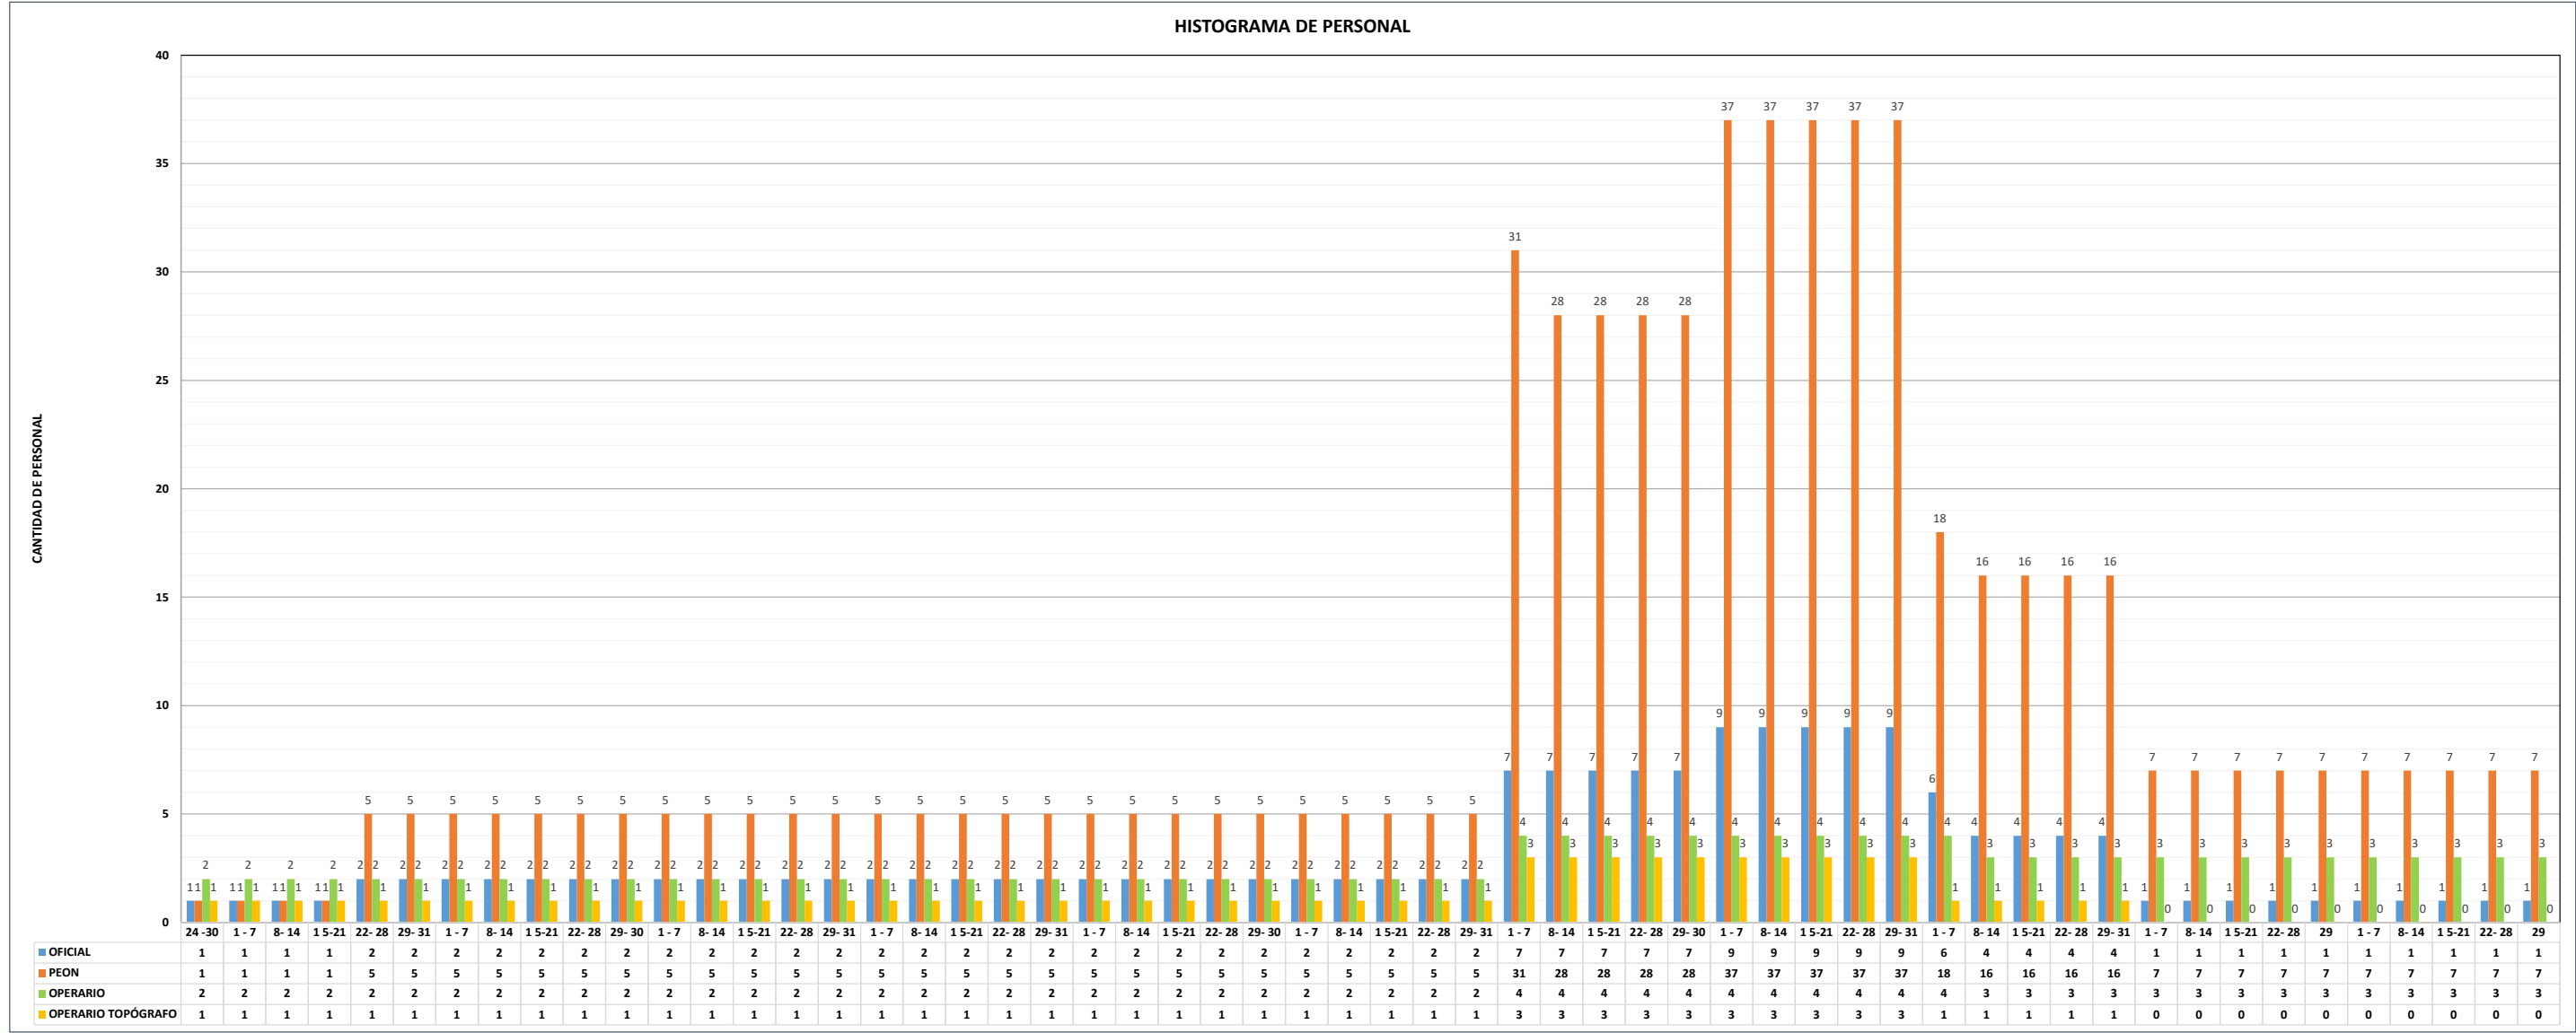


[illegible]

CRONOGRAMA "SERVICIO DE SUMINISTRO DE VEGETACIÓN Y PLANTACIÓN – RÍO LACRAMARCA"			CUADRO RESUMEN DE PERSONAL Y EQUIPO																																																			
			2023																														2024																					
			ABRIL		MAYO				JUNIO				JULIO				AGOSTO				SETIEMBRE				OCTUBRE				NOVIEMBRE				DICIEMBRE				ENERO			FEBRERO			MARZO											
PERSONAL Y EQUIPO		MÁXIMO	24-30	1-7	8-14	15-21	22-28	29-31	1-7	8-14	15-21	22-28	29-30	1-7	8-14	15-21	22-28	29-31	1-7	8-14	15-21	22-28	29-30	1-7	8-14	15-21	22-28	29-31	1-7	8-14	15-21	22-28	29-30	1-7	8-14	15-21	22-28	29-31	1-7	8-14	15-21	22-28	29	1-7	8-14	15-21	22-28	29						
PERSONAL																																																						
OFICIAL	9		9	1	1	1	1	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	7	7	7	7	7	7	9	9	9	9	9	6	4	4	4	4	1	1	1	1	1	1	1	1	1
PEON	37		37	1	1	1	1	5	5	5	5	5	5	5	5	5	5	5	5	5	5	5	5	5	5	5	5	5	5	31	28	28	28	28	37	37	37	37	37	37	18	16	16	16	16	7	7	7	7	7	7	7	7	7
OPERARIO	4		4	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	4	4	4	4	4	4	4	4	4	4	4	3	3	3	3	3	3	3	3	3	3	3	3	3	3	
OPERARIO TOPÓGRAFO	3		3	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	3	3	3	3	3	3	3	3	3	3	3	1	1	1	1	1	0	0	0	0	0	0	0	0	0
EQUIPO																																																						
ESTACION TOTAL	3		3	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	3	3	3	3	3	3	3	3	3	3	3	0	0	0	0	0	0	0	0	0	0	0	0	0	
MINI CARGADOR (A TODO COSTO)	4		4	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	4	4	4	4	4	4	4	4	4	4	4	2	2	2	2	2	2	2	2	2	2	2	2	2		
VOLQUETE (A TODO COSTO)	4		4	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	2	4	4	4	4	4	4	4	4	4	4	4	2	1	1	1	1	1	1	1	1	1	1	1	1	1	
CAMION CISTERNA (3,500 GLNS - MAQ. SECA)	3		3	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	
FUNGIDORA	3		3	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1		

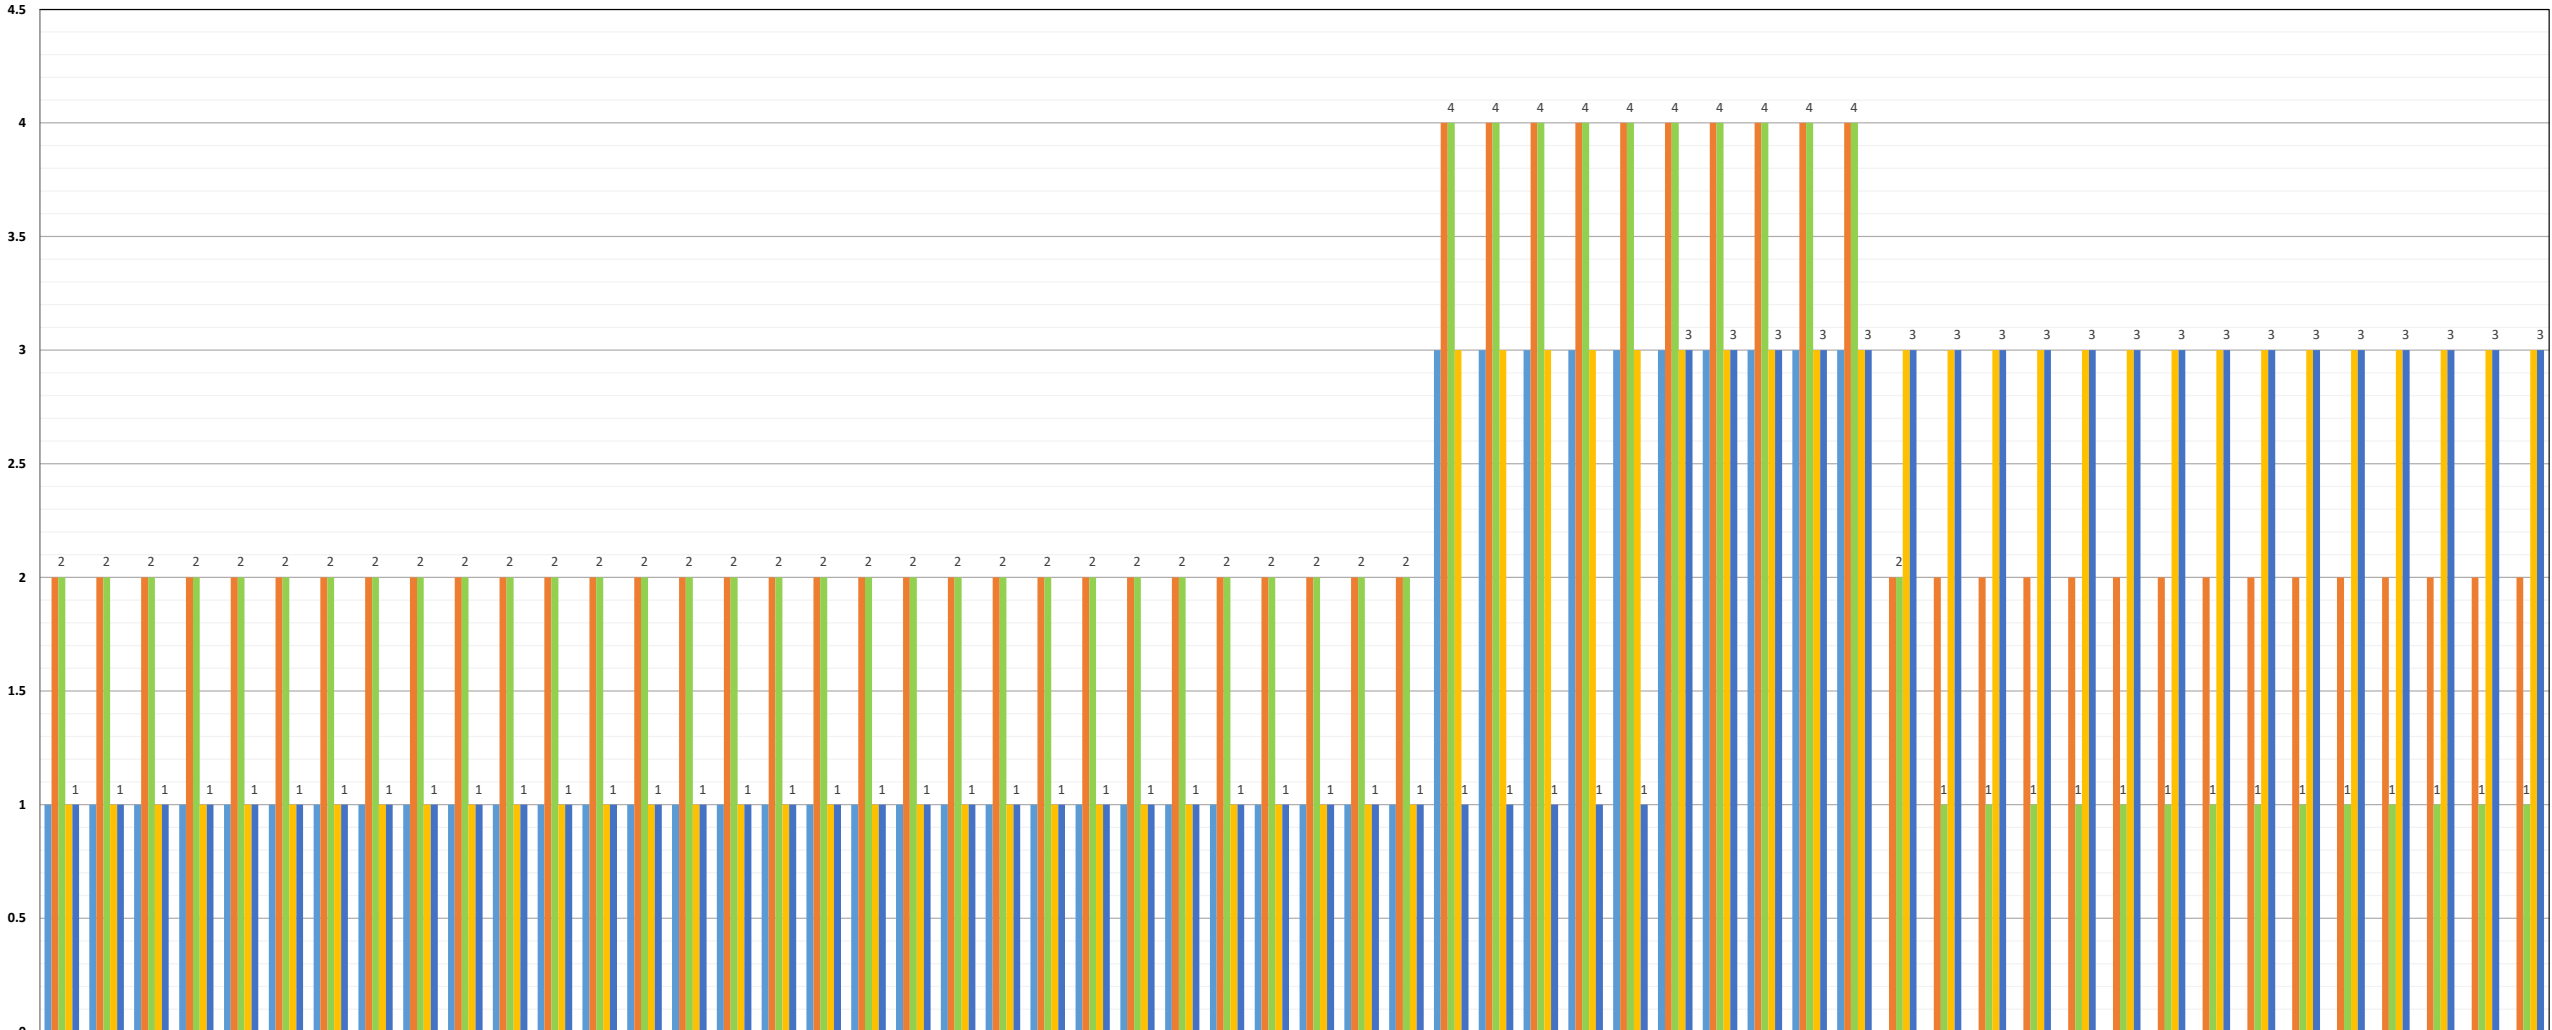

HISTOGRAMA DE EQUIPOS

[illegible]
